Akelius - MenoMali Schools project, 2025-2033

Bamabougou, June 2026

Village of Bamabougou

village and seat of the *Commune Diedougou Tourodo*.

- population, 1540 inhabitants
- children aged 0 to six, 438
- children aged seven to twelve,197

- pupils attending the first cycle, age 6 to 12, total 175
- expected number of pupils to be enrolled for next school year 2026-2027, total 60

present school buildings

- school built by the state
- one building with three classrooms
- all classrooms have crumbling or destroyed false ceilings

- two latrines gender separated for the students
- insufficient number of school desks
- no water well serving the school

education

- three teachers paid by the state, on average one teacher has 60 students.
- school material is not sufficient

new school buildings

The buildings planned for the new schools are

- three classrooms, each with a capacity of fifty students
- one library
- three teachers' apartments

- one kitchen
- one storage room
- two latrines block gender separated for the school

- one latrine block gender separated for the teachers
- one water well
- one amphitheater

The project includes the renovation of the existing school building with the construction of a new roof.

actual school buildings

the new school

total area made available for the school, 26,000 square meters

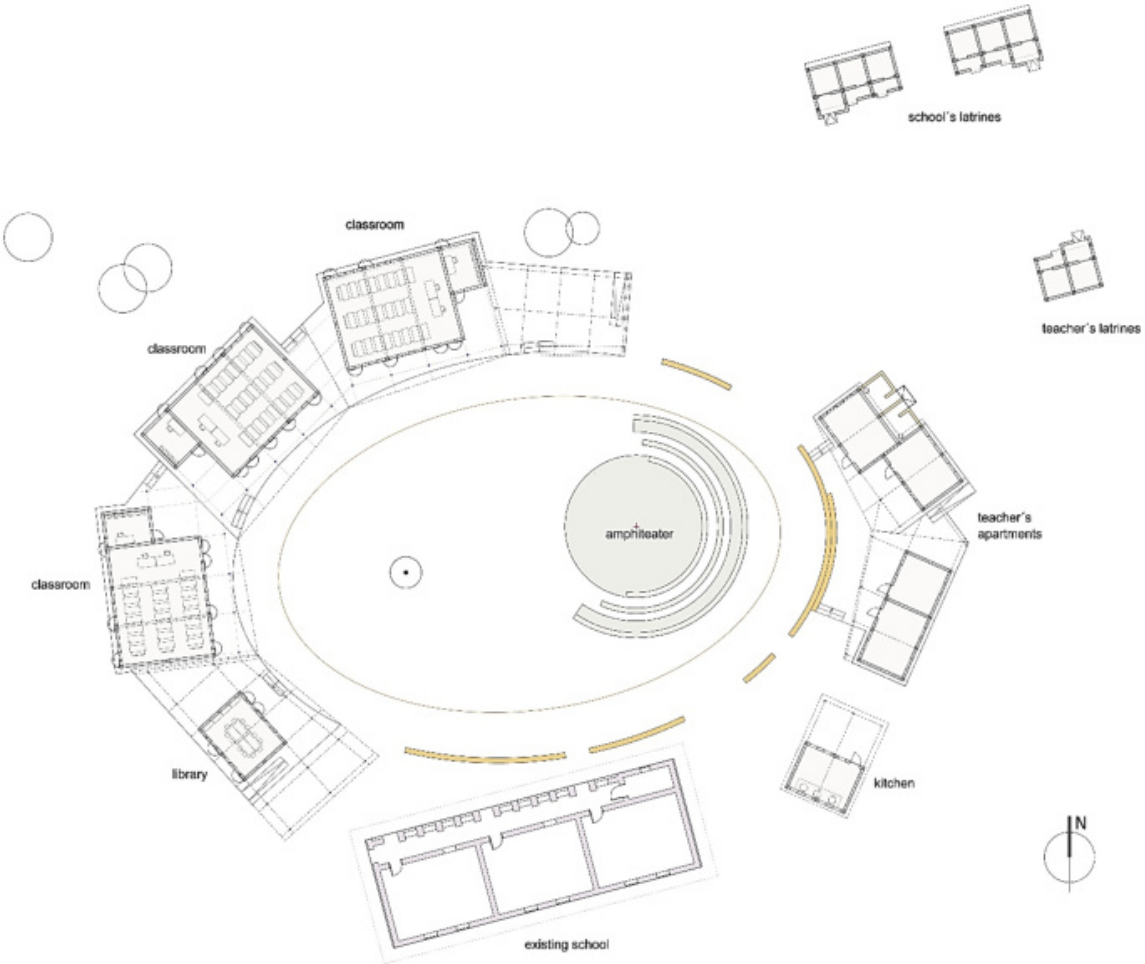

site plan

construction of the water well

the drilling truck arrives at the village

drilling works

Drilling work takes three days.
The aquifer is encountered with the following parameters

Depth, 60 meters
Water flow rate, 2,45 m3/h

placement of the school´s buildings

the village clean the school site

marking of the school plan

the foundations are dug

construction materials arrive at the site

preparation of reinforcement elements for the foundations

construction of the foundation

foundation reinforcement

construction of the foundation ring beam for the classrooms and the library

construction of the foundation ring beam for the teacher´s apartments and the kitchen.

contruction of the walls

classrooms, back view

classrooms, front view

Once the foundation beam is completed, the construction of the walls begins

teacher’s apartment, front view

teacher’s apartment, back views

Construction is progressing rapidly.
The teachers' apartments have already reached roof level.
